



Look for all future News about  
your residence on the website  
[www.uflats.com](http://www.uflats.com)

*July 28, 2006*

For information about  
CLOSINGS / MOVE-INS,  
contact your  
Sales Representative:  
Jenny 612-205-2550  
Ryan 952-484-9644  
Seth 612-328-1825



## **CHUCK'S CORNER – EXXXPANDED**

### **EXTERIOR**

- Garage concrete floor is poured and garage doors are installed
- Wirsbo heating in pavement on garage approach is complete
- Main entry doors to be installed in two weeks
- Brick is 80% complete; Stucco is 40% done
- Decks will be completed the first week of August

### **INTERIOR**

- Drywall is complete with taping 98% done
- Laminate Countertops are complete on 4<sup>th</sup> and 3<sup>rd</sup>
- Cabinets and hardware are installed on 4<sup>th</sup>, 3<sup>rd</sup>, and half of 2<sup>nd</sup>
- Ceramic Tile is installed on 4<sup>th</sup> and 3<sup>rd</sup>
- Wood Floors are installed on 4 and some on 3<sup>rd</sup>
- Carpet will begin installation on 4<sup>th</sup> on Aug 3rd
- Appliances have been delivered on 4<sup>th</sup>
- Door Frames are being installed on 4<sup>th</sup>
- Electrical Fixtures are being installed on 4<sup>th</sup> and 3<sup>rd</sup>
- Plumbing Fixtures are installed on 4
- Common Area Finishes are 90% selected.
- Permanent power is expected Aug 3<sup>rd</sup> with Elevator installation to follow

There is a definite rhythm and momentum happening at 2600 University! The crews are working diligently in hot temperatures and long days! The Pizza Wagon visited the site and treated all the workers to pizza and freshly baked chocolate chip cookies!! Yummy!

## ...What's Happening On-Site




**Unit 421** – Patio door frame going in.



**Unit 420** – Countertop being measured.



**Unit 112** – Gyp-crete being poured.



**Unit 316** – View from deck!



Electrician boys wiring in the basement.




**Unit 113** – Carpenters framing up the patio door.



**Unit 421** – Countertops and wood floors are in!



**Unit 304** – Tile set in the master bath.

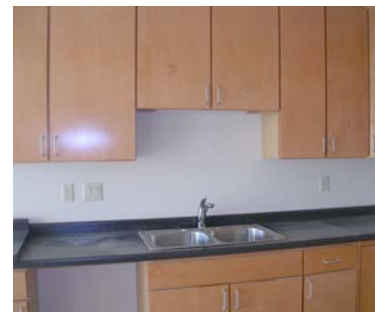

**Unit 419** – Kitchen countertop and sink are in!



**Unit 301** – Kitchen cabinets installed.
